

MEMORANDUM FOR: Director of Special Projects

SUBJECT

: Photo Reconnaissance Systems Report No. 28

I. **CORONA**

A. Accomplishments

- 1. The PIM Meeting, convened 17-18 February at the A/P, resulted in excellent information exchange among CORONA program participants.
- 2. The 18 February meeting reviewed the problem of system incompatibility with UTB payloads and concluded that deletion of UTB from the CORONA Program was the best course of action.
- 3. The initial audit of CR-10 on 19 February indicates that the system will be ready for launch on 4 March.
- 4. AWA's 1, 2, 3, 4 and 6 were negotiated with the A/P on 13 February, for a total of including of 28, 985 man-hours of labor were added to the contract.

B. Problems

- 1. Tracking problems arising from the use of UTB film resulted in the cancellation of the CR-II flight, scheduled for 18 February. CR-11 is being refitted for use with STB and is rescheduled for the next flight, currently scheduled for 6 May.
- 2. P/L tracking problems with UTB, similar to those observed in CR-11, have occurred during cycling of CR-12 and CR-13. These units will also be refitted with STB, with no impact on the current


Declassified and Released by the transfer of the last transfer of transfer of the last transfer of transfer of the last transfer of tra	· ·
on	
Declassified and Heleased by 185 (4.1.0	


In Appendiance with E.O. 12958




C. Projected Status

- 1. CR-10. Flight preps.
- 2. CR-11. Special tests/conversion to STB.
- 3. CR-12. Conversion to STB.
- 4. CR-13. Environmental preps.
- 5. QR-2. Subsystem testing.
- 6. CR-14. Receiving and inspection.

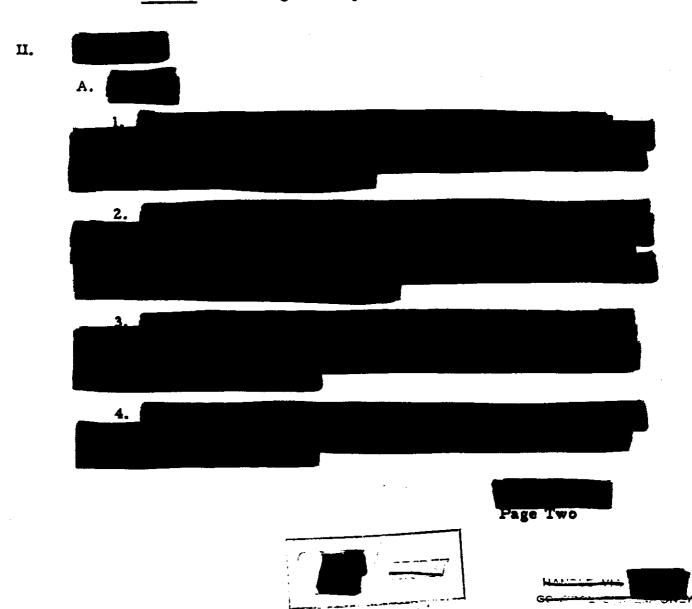


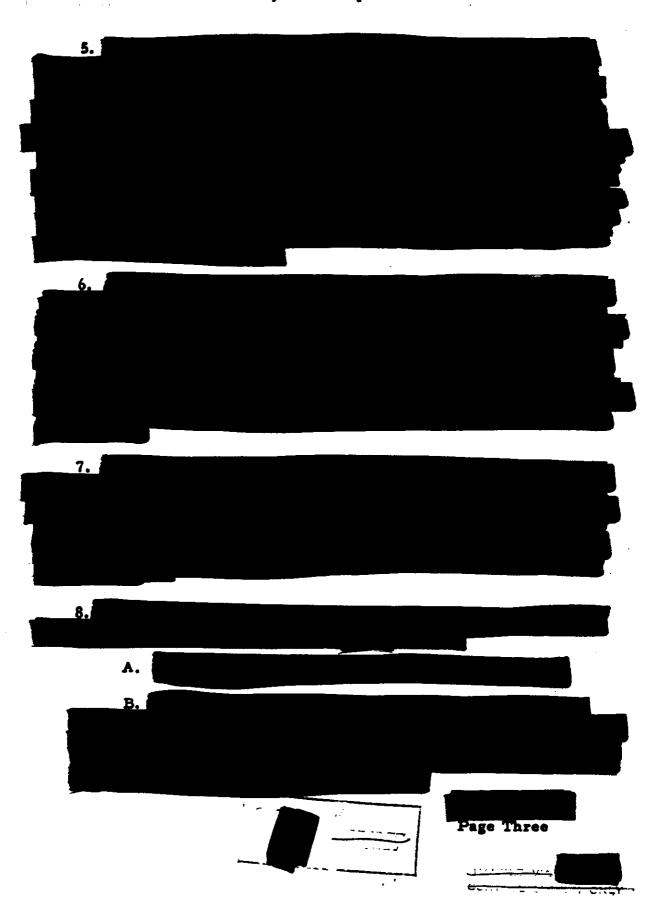



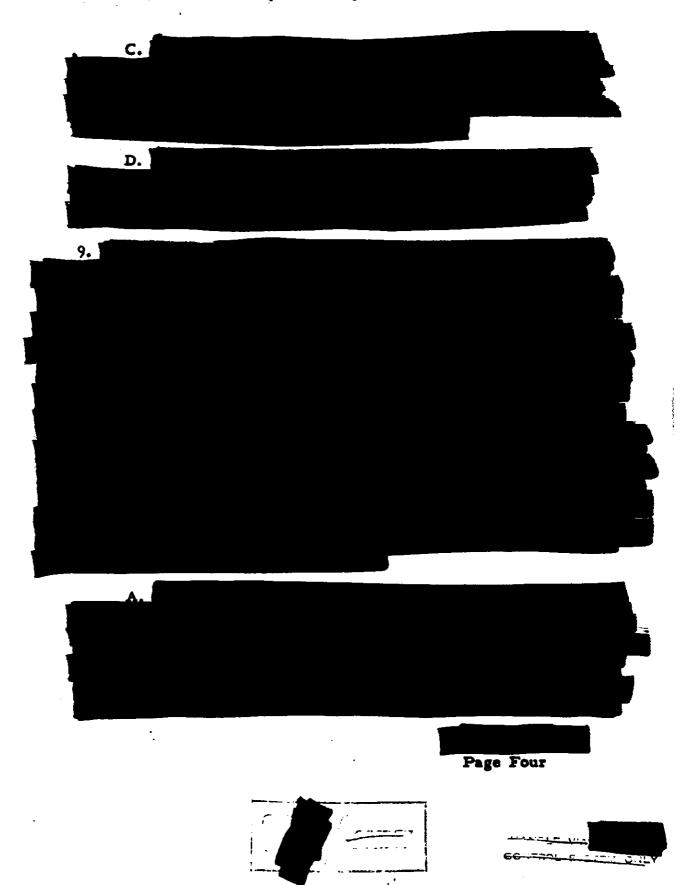



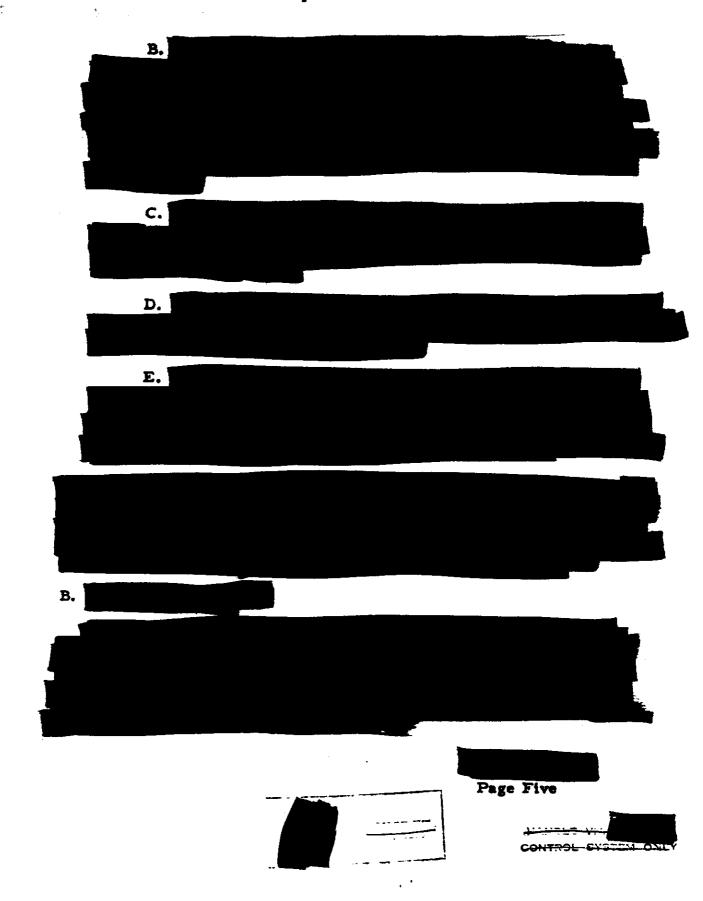

E EEEE


SUBJECT: Photo Reconnaissance Systems Report No. 28

III.

2. 3.

GENTIOL EVETTY ONLY

Page Six

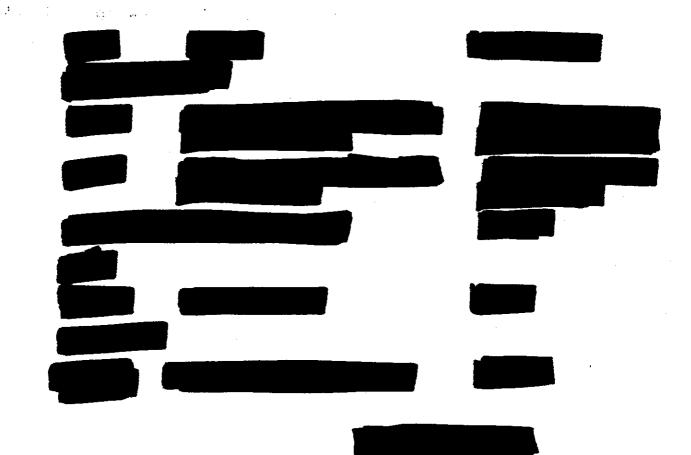

Distribution:



Page Seven

PANTLE VIA
