

ROUTE SHEET
NDW-NRL-5216/1552

CODE		TIALS	*PUR-POSE	REMARKS
7032.23	8/23/77	V.N.		(for review)
7032	8/23	Fug		
7033	8/23	PAH		
7033A	8/24	Tch		
7030	8/23	SMT (acting)		
7030A	8/24	clde		
9110				
106-51		X		

POPPY TERMINATION

INSTRUCTIONS

Prepare 2 copies of this route sheet and forward ALL copies together with necessary correspondence and other documents.

*PURPOSES

- 1. FOR INFORMATION
- 2. FOR APPROVAL
- 3. PREPARE REPLY
- 4. PREPARE ENDORSEMENT
- 5. FOR NECESSARY ACTION
- 6. FOR SIGNATURE
- 7. RETAIN ENCLOSURE
- 8. RETAIN COPY

FROM

Code 7030

DATE OF MATERIAL

22 Aug 1977

BRANCH IDENT. SYMBOL

7032-408:VTN:d1m

ORIG. IDENT. SYMBOL (Mail Room Fill in)

DIVISIONS DO NOT FILL IN

DATE MAILED

FILE NO.

SUBJECT

Siss Zulu (P-1) Deinstallation

HANDLE VIA
BYEMAN
CONTROL SYSTEM ONLY

R/S NO. (Mail Rm. Fill in)

OPTIONAL FORM NO. 10
JULY 1973 EDITION
GSA FPMR (41 CFR) 101-11.6~~SECRET~~

UNITED STATES GOVERNMENT

Memorandum

TO : Code 9110

7032-408:VTN:dlm
DATE: 22 August 1977

FROM : Code 7030

SUBJECT: Siss Zulu (P-1) Deinstallation

Ref: (a) Cite SPO 0569, DTG 011902Z August 1977

Encl: (1) Cost Estimate of Deinstallation
(2) Schedule of Deinstallation

1. As requested in reference (a), enclosures (1) and (2) are provided herewith.

2. It should be noted that the original deinstallation guidelines were modified to reduce the overall costs of this task. The cost savings amounted to \$195,857.00.

LEE M. HAMMARSTROM, Acting Manager,
Advanced Projects Office

5010-110

~~SECRET~~

U.S. Savings Bonds Regularly on the Payroll Savings Plan

HANDLE VIA
SYSTEM ONLY

~~SECRET~~COST ESTIMATE FOR P-1 DEINSTALLATION

NOTE: ☐ system intact for reinstallation. Antennas and towers to be left in their present location. Internal/external cabling pulled outside and coiled up on the ground. Cable entry/exit ports to be filled in. P-1 OPS room to be completely cleared. The technical power will be removed back to the distribution panel.

☐ system to be surveyed and only those items to be identified by Code 7032 will be returned to NRL

ITEM	SITE		REMARKS
I. Material Costs	\$ 5,048.00	\$ 939.75	
II. Material Shipment	3,130.00	875.00	15,650 lbs/2500 lbs
III. Salary	32,880.00	12,480.00	240/mda ☐ 9 men ☐ 6 men)
IV. Per Diem	7,497.00	1,875.00	
V. Travel	7,907.00	5,616.00	\$748/rt-local=\$200-car rental \$975 (\$936/rt
VI. Consignment	1,000.00	500.00	
VII. Equipment Shipment	5,200.00	4,390.00	2 40ft vans at ☐ Green sheet at ☐
TOTAL	62,662.00	26,675.75	

TOTAL COST OF DEINSTALLATION \$89,337.75

Enclosure (1) to NRL Memo
7032-408:VTN:d1m
22 August 1977

HANDLE VIA
SQUAD
CONT. SYSTEM ONLY

~~SECRET~~

SECRET


P-1 DEINSTALLATION SCHEDULE

15 August 1977

C05026501

Approved for Release: 2024/06/14 C05026501

Approved for Release: 2024/06/14 C05026501

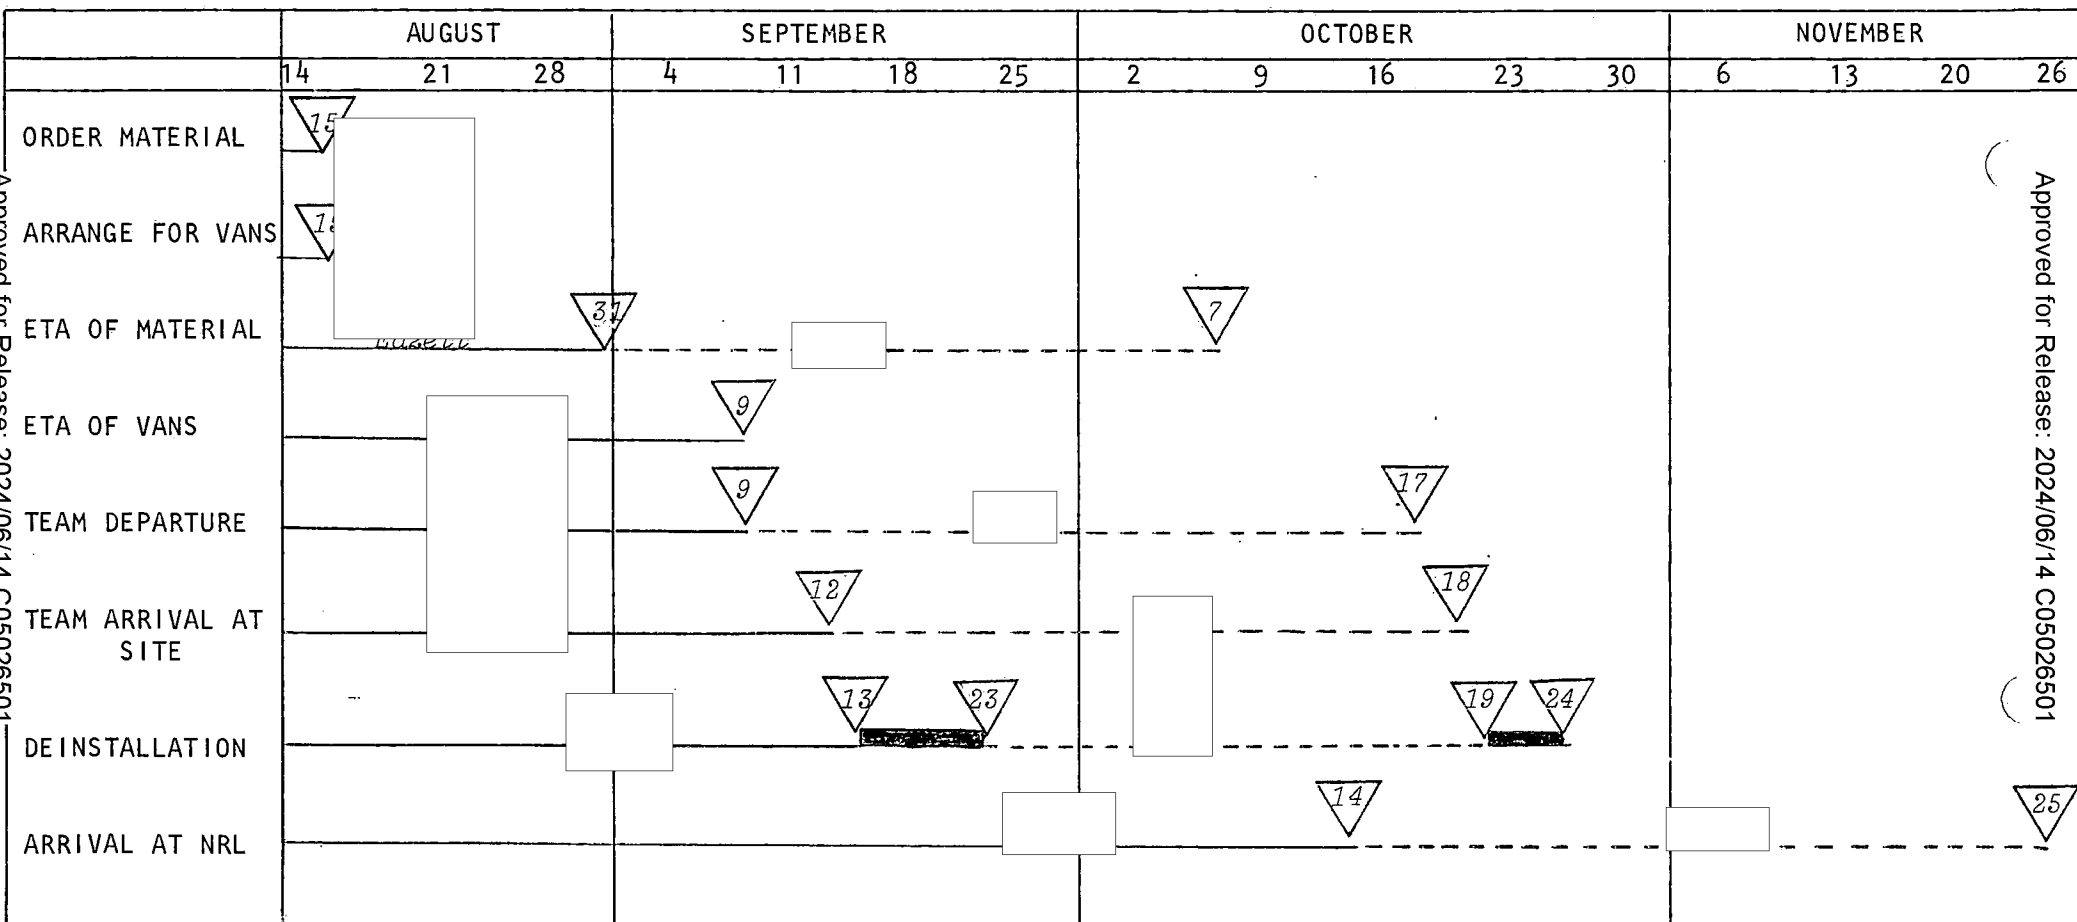

SECRET

Enclosure (2) to Memo
7032-408:VTN:d1m
22 August 1977
HANDLE VIA
BYEMAN
CONTROL SYSTEM ONLY
