Copy
5 December 1969

MEMORANDUM FOR: Director of Special Projects

SUBJECT: Photo Reconnaissance Systems Report No. 17

I. **CORONA**

A. **Accomplishments**

1. **CR-9.** V/H programmer originally in CR-9 was returned to AP. Physical examination revealed that the stepper switch was slipping on its shaft. Special test made with the new programmer in CR-9 confirmed successful operation, no problems. Launch successful on 4 December.

2. **CR-11.** Completed vibration. Waiting for evaluation of Dr. A. from HIVOS tests.

3. **CR-10.** Block test results are being evaluated. The SO-242 exposure run has been forwarded to ████████████ for review.

4. **CR-13.** Completed acceptance testing.

B. **Problems**

V/H programmers. All programmers in this facility are being disassembled to ensure correct screw adjustment and shaft smoothness. Component level tests will be completed prior to installation in any system.

C. **Projected Status**

1. **CR-9.** Mission 1108 4-24 December.

2. **CR-10.** Resolution block testing.

GROUP 1
Excluded from automatic
downgrading and
declassification

SUBJECT: Photo Reconnaissance Systems Report No. 17

   3. <u>CR-11.</u> Evaluation of HIVOS data.

   4. <u>CR-12.</u> Pre-HIVOS preparations.
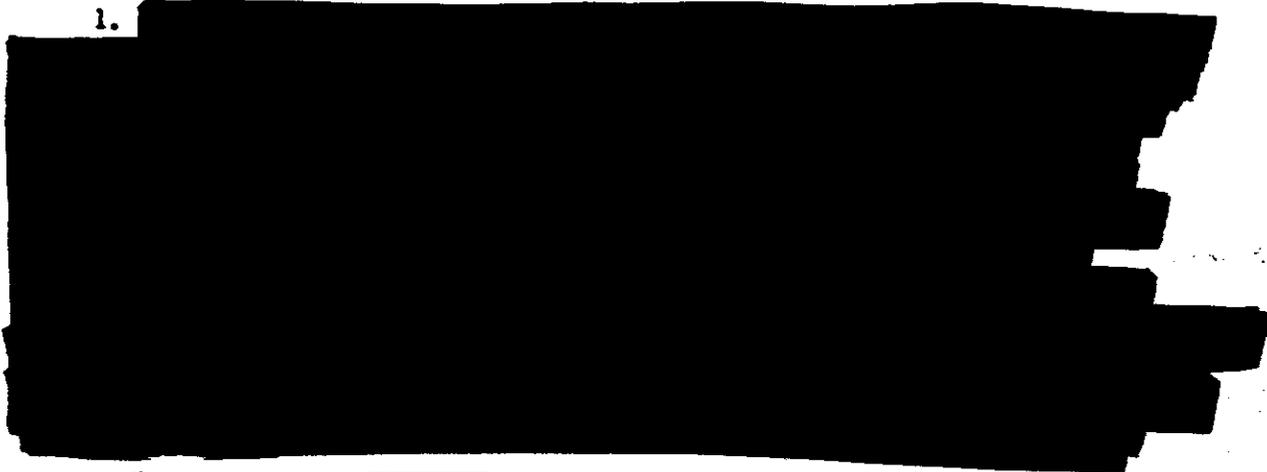
   5. <u>CR-13.</u> Functional testing.

II. ████████

   A. ████████

      1. ██

      2. ██

      3. ██

      4. ██

NOTICE OF REMOVED PAGES

Pages_____3____through____6_____ are not provided because their full text does not contain CORONA, ARGON, LANYARD programmatic information.
